JOB: 13004 Rte. F Relocation, Oak Grove, MO J4P2267

S	M	Description	Phase	Cat	Start Date	Finish Date	Days
		Rte. F Relocation, Oak Grove, MO J4P2267	1		7/24	10/31	333
		Initial Survey Layout	1		7/24	7/24	1
		Initial Traffic Control Set up	1		8/1	8/1	1
		Mobilization	1		8/5	8/5	1
		Staging Area Set up	1		8/5	8/7	3
		Initial Erosion Control Installation	1		8/7	8/7	1
		Waterline Relocation Start @ WL Sta. 5+00	1		8/8	2/3	128
		General Clearing and Grubbing	1		8/8	8/21	10
		Removals needed to install waterline and Storm Sewer	1		8/8	3/19	160
		Grp B Pipe, DI, MH, installation @ Sta 9+64.52 on E&W sides	1		8/22	4/2	160
		Grp A Drainage Crossing 1 @ Sta 17+11.91	1		9/13	9/13	1
		Slotted Drain 1 install Sta 18+59.06 to 19+04.06	1		9/17	9/18	2
		Type B Collar	1		9/23	9/23	1
		Waterline Encasement 1 WL Sta. 12+53	1		9/20	9/20	1
		Waterline Encasement 2 Sta 17+52.66	1		9/27	9/27	1
		Waterline Encasement 3 Sta. 21+33.53	1		10/4	10/4	1
		Slotted Drain 2 Install @ Sta 23+83.29 to 23+93.29	1		10/1	10/2	2
		Clearing and Grubbing East side of culvert end	1		10/9	10/10	2
		10'x5'x135.14' RCB @ Sta. 27+20.45	1		10/10	10/23	10
		Waterline Encasement 4 Sta. 32+83	1		10/25	10/25	1
		Waterline Encasement 5 Sta. 38+74	1		11/1	11/1	1
		Clearing and Grubbing Culvert East Ends	1		11/15	11/18	2
		9'x6'x113.94' RCB @ Sta 41+00.24	1		11/18	11/29	10
		Waterline Encasement 6 Sta. 43+09	1		11/8	11/8	1
		Type A Pipe Collar 48" Tie in Sta. 48+69.97	1		11/15	11/15	1
		Waterline Encasement 7 @ Sta. 53+22	1		11/15	11/15	1
		Grp A Drainage Crossing 2 @ Sta. 60+78.65	1		11/29	11/29	1
		Grp A Drainage Crossing @ Sta. 74+64	1		12/13	12/13	1
		Grp A Drainage Crossing @ Sta 81+53.64	1		12/27	12/27	1
		Waterline Encasement 8 @ Sta. 83+35	1		12/27	12/27	1
		Grp A Drainage Crossing @ Sta. 84+46.45	1		1/2	1/2	1
		Grp A Drainage Crossing @ Sta. 91+55.98	1		1/14	1/14	1
		Watermain Tie in at S. Clinton St.	1		2/6	2/6	1
		Watermain Tie in at Alley off of 13th St.	1		2/6	2/6	1
		Watermain Tie in at 14th St.	1		2/7	2/7	1
		Watermain tie in @ 15th St.	1		2/7	2/7	1
		Watermain Tie in @ 16th St.	1		2/7	2/7	1
		Watermain Ti in @ 18th St.	1		2/10	2/10	1
		Watermain Tie in at 19th St.	1		2/10	2/10	1
		Watermain Tie in at Sta. 38+74	1		2/10	2/10	1
		Watermain Tie in at Sta. 21st St.	1		2/10	2/10	1
		Watermain Tie in at Sta. 22nd St	1		2/11	2/11	1
		Watermain Tie in at 24th St.	1		2/11	2/11	1
		Watermain Tie in at 25th St.	1		2/11	2/11	1
		Watermain Tie in at 30th St.	1		2/11	2/11	1
		Temporary Striping	1		3/20	3/20	1
		Removal of Improvements	1		8/8	7/23	250
		Stage 1 Unclassified Excavation for Outer lanes	1		3/20	4/28	28
		Embankment in Place mainly around Sta 59+00 area.	1		4/8	4/28	15
		Compacting Embankment	1		4/8	4/30	17
		Modified Subgrade	1		4/1	6/23	60
		Stage 1 outer lane Type 1 Base Rock Placement	1		5/5	6/20	35
		Stage 1 outer lane 8.5" PCCP Paving	1		5/6	7/28	60
		Temporary Bypass Construction	1		6/23	6/26	4
		Driveway Construction	1		4/1	7/21	80
		MSE Wall Construction	1		4/10	4/23	10
		Sound Wall Construction	1		4/7	4/18	10
		MSE and Sound Wall Coating	1		4/24	4/28	3
		Side street Tie ins	1		5/8	7/25	57
		Curb and Gutter Construction	1		7/28	8/26	22
		Inlet Throats	1		7/30	8/22	18
		Curb Ramps and ADA Domes	1		4/28	5/27	22

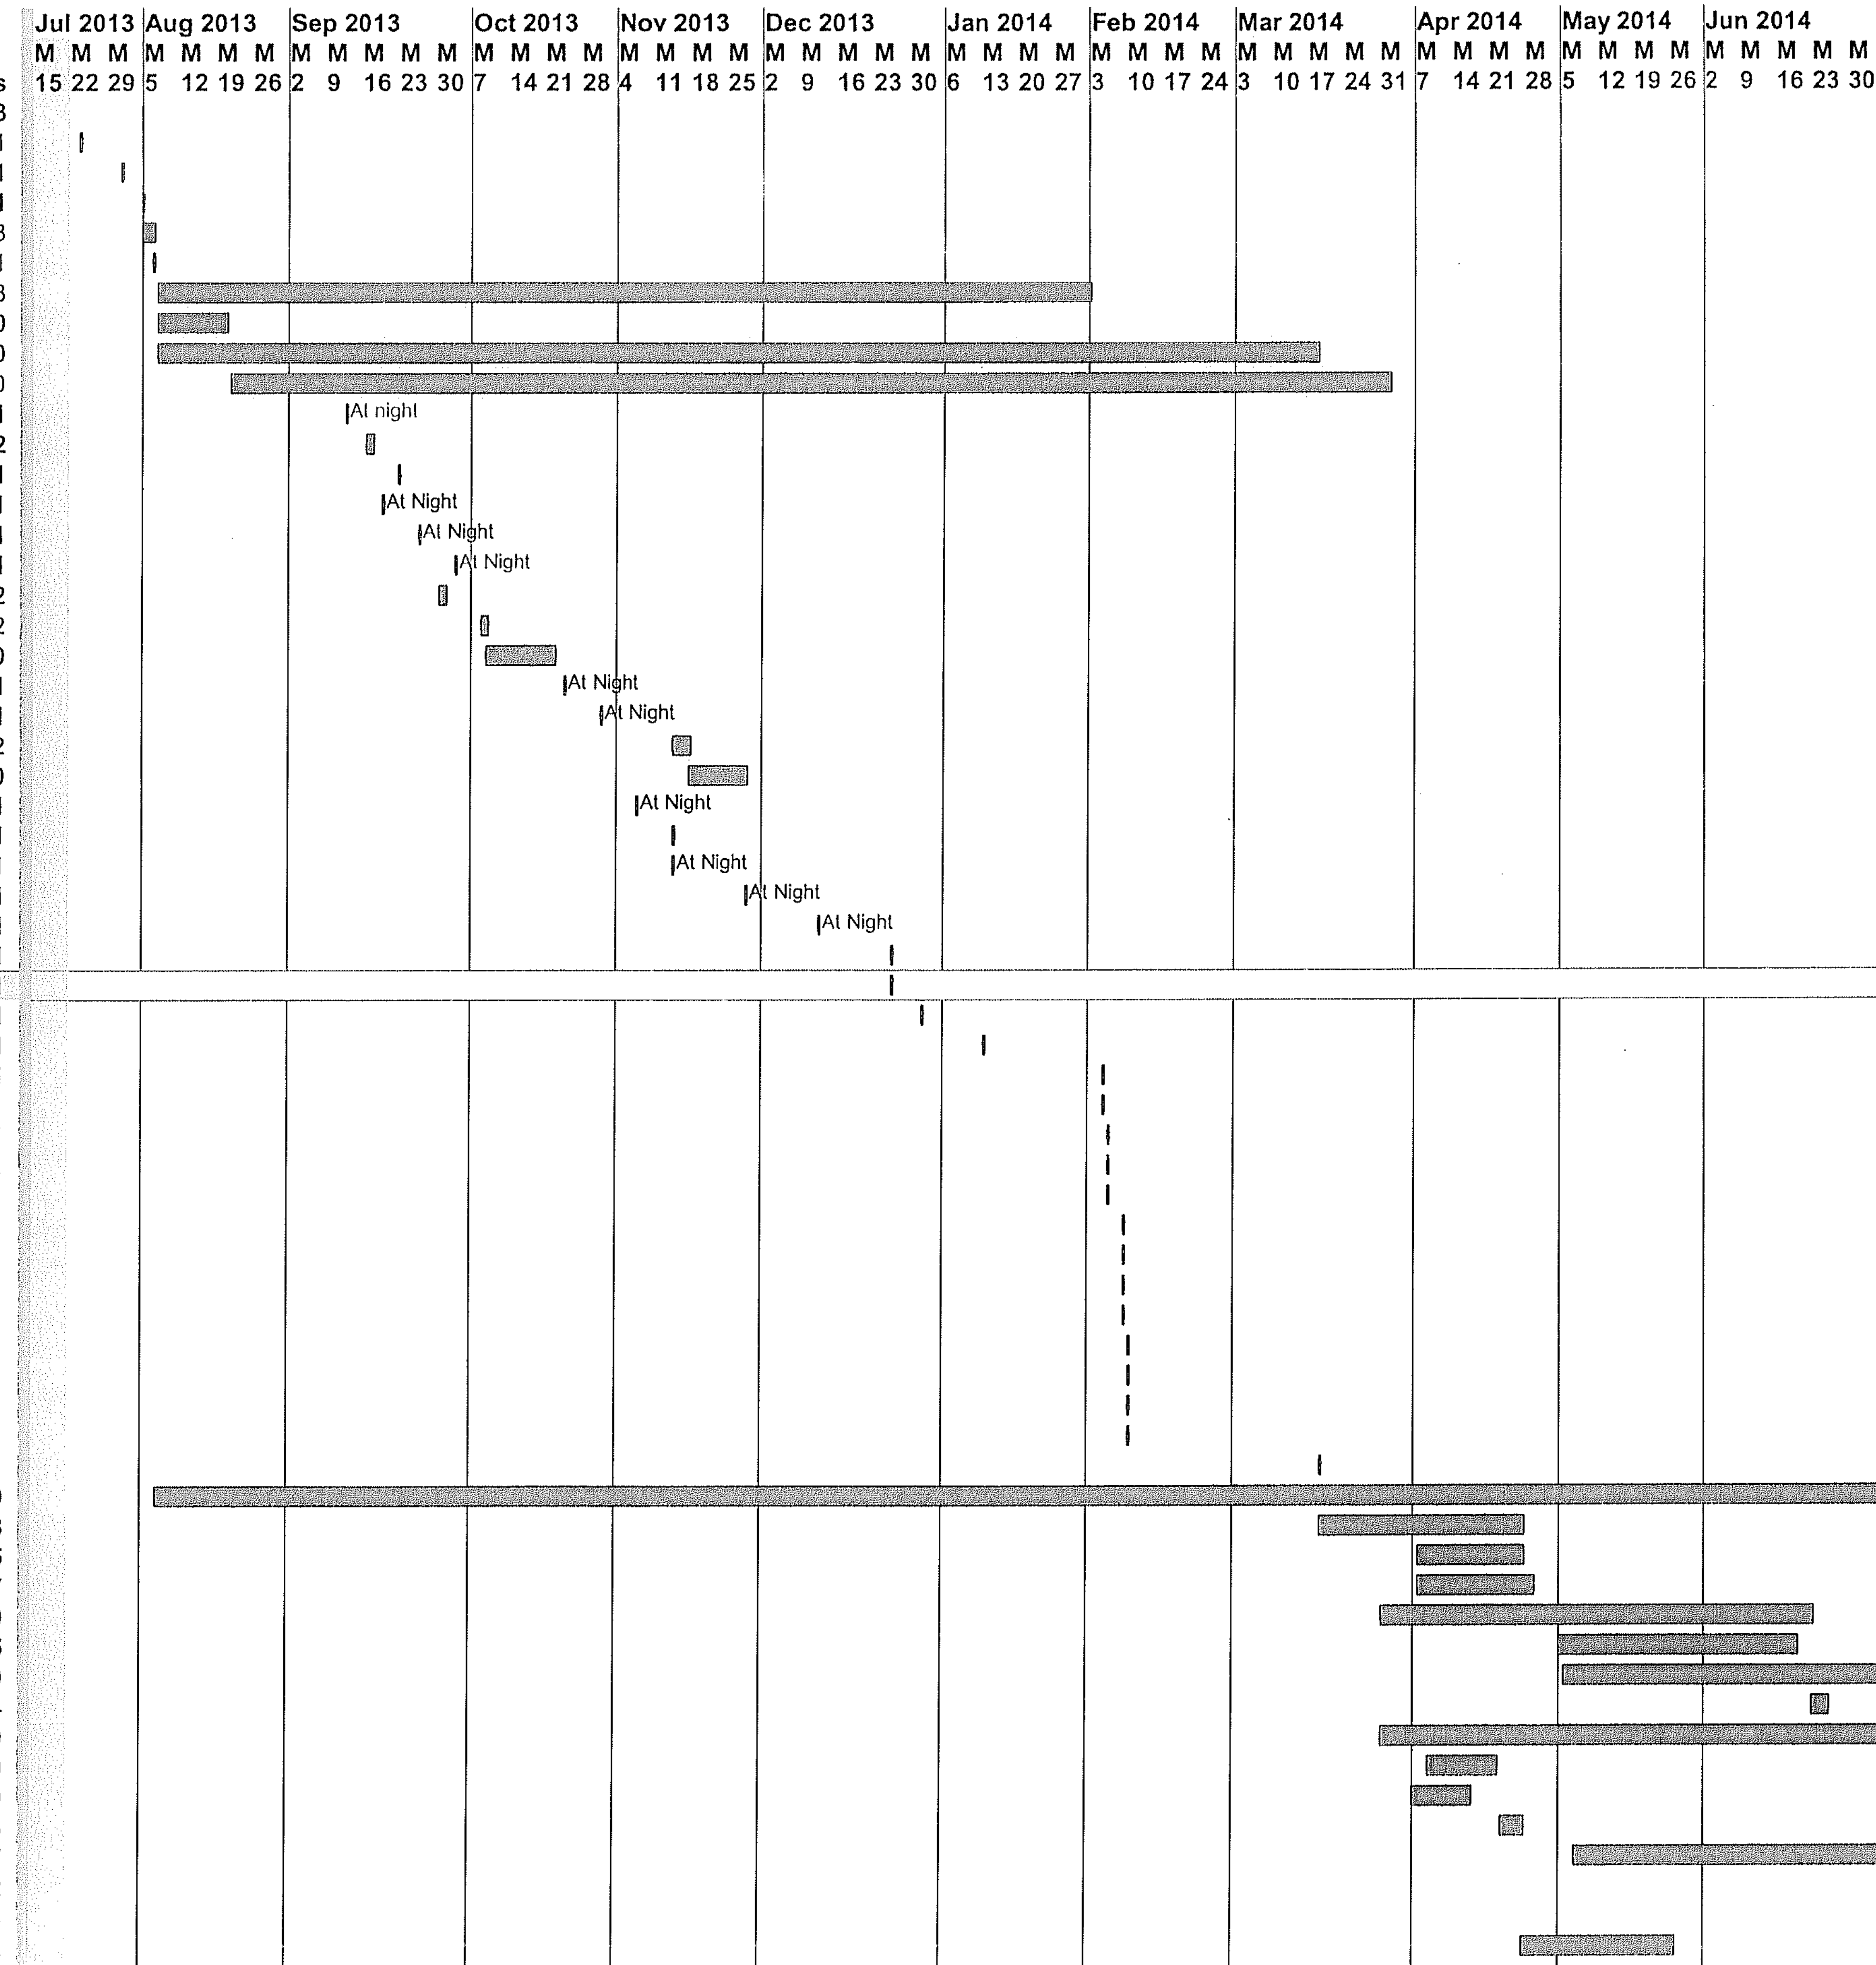

JOB: 13004 Rte. F Relocation, Oak Grove, MO J4P2267

Jul 2014	Aug 2014	Sep 2014	Oct 2014	Nov 2014	Dec 2014	Jan 2015	Feb 2015	Mar 2015	Apr 2015	May 2015	Jun 2015	Jul 2015	Aug 2015	Sep 2015	Oct 2015	Nov 2015	Dec 2015	Jan 2016	Feb 2016	Ma
M M M M	M M M M	M M M M M	M M M M	M M M M	M M M M M	M M M M	M M M M	M M M M M	M M M M	M M M M	M M M M M	M M M M	M M M M M	M M M M	M M M M	M M M M M	M M M M	M M M M	M M M M M	M
7 14 21 28	4 11 18 25	1 8 15 22 29	6 13 20 27	3 10 17 24	1 8 15 22 29	5 12 19 26	2 9 16 23	2 9 16 23 30	6 13 20 27	4 11 18 25	1 8 15 22 29	6 13 20 27	3 10 17 24 31	7 14 21 28	5 12 19 26	2 9 16 23 30	7 14 21 28	4 11 18 25	1 8 15 22 29	7

Note JSP V and X Precaution's

JOB: 13004 Rte. F Relocation, Oak Grove, MO J4P2267

S	M	Description	Phase	Cat	Start Date	Finish Date	Days
		Sidewalk Construction	1		4/30	6/6	28
		Retaining Walls	1		5/6	5/21	12
		Finish Grade Greenways	1		8/18	8/26	7
		Seed and Mulch Stage 1 Areas	1		8/27	8/29	3
		Switch Traffic to outer lanes for Stage 2	2		8/29	8/29	1
		Temporary Traffic Barrier	2		8/29	10/14	33
		Stage 2 Unclassified Excavation	2		8/29	9/11	10
		Compacting in Cut	1		8/29	9/25	20
		Stage 2 Type 1 Base Rock	2		9/25	10/6	8
		Stage 2 8.5" PCCP Paving	2		9/29	10/8	8
		Type A3 Shoulders	2		10/9	10/10	2
		Remove Temp Bypass	2		10/13	10/14	2
		Remove Temporary Barriers	2		10/14	10/14	1
		Electrical at Crosswalks	3		9/22	10/22	23
		Chainlink Fence at RCB ends	3		4/21	4/21	1
		Guardrail Installation	3		10/15	10/22	6
		Removal of Temp striping and Install New	3		10/15	10/24	8
		Signing	3		10/20	10/24	5
		Finsh Seeding and Mulching	3		10/27	10/29	3
		Cleanup	3		10/20	10/30	9
		Open entire road to public	3		10/31	10/31	1

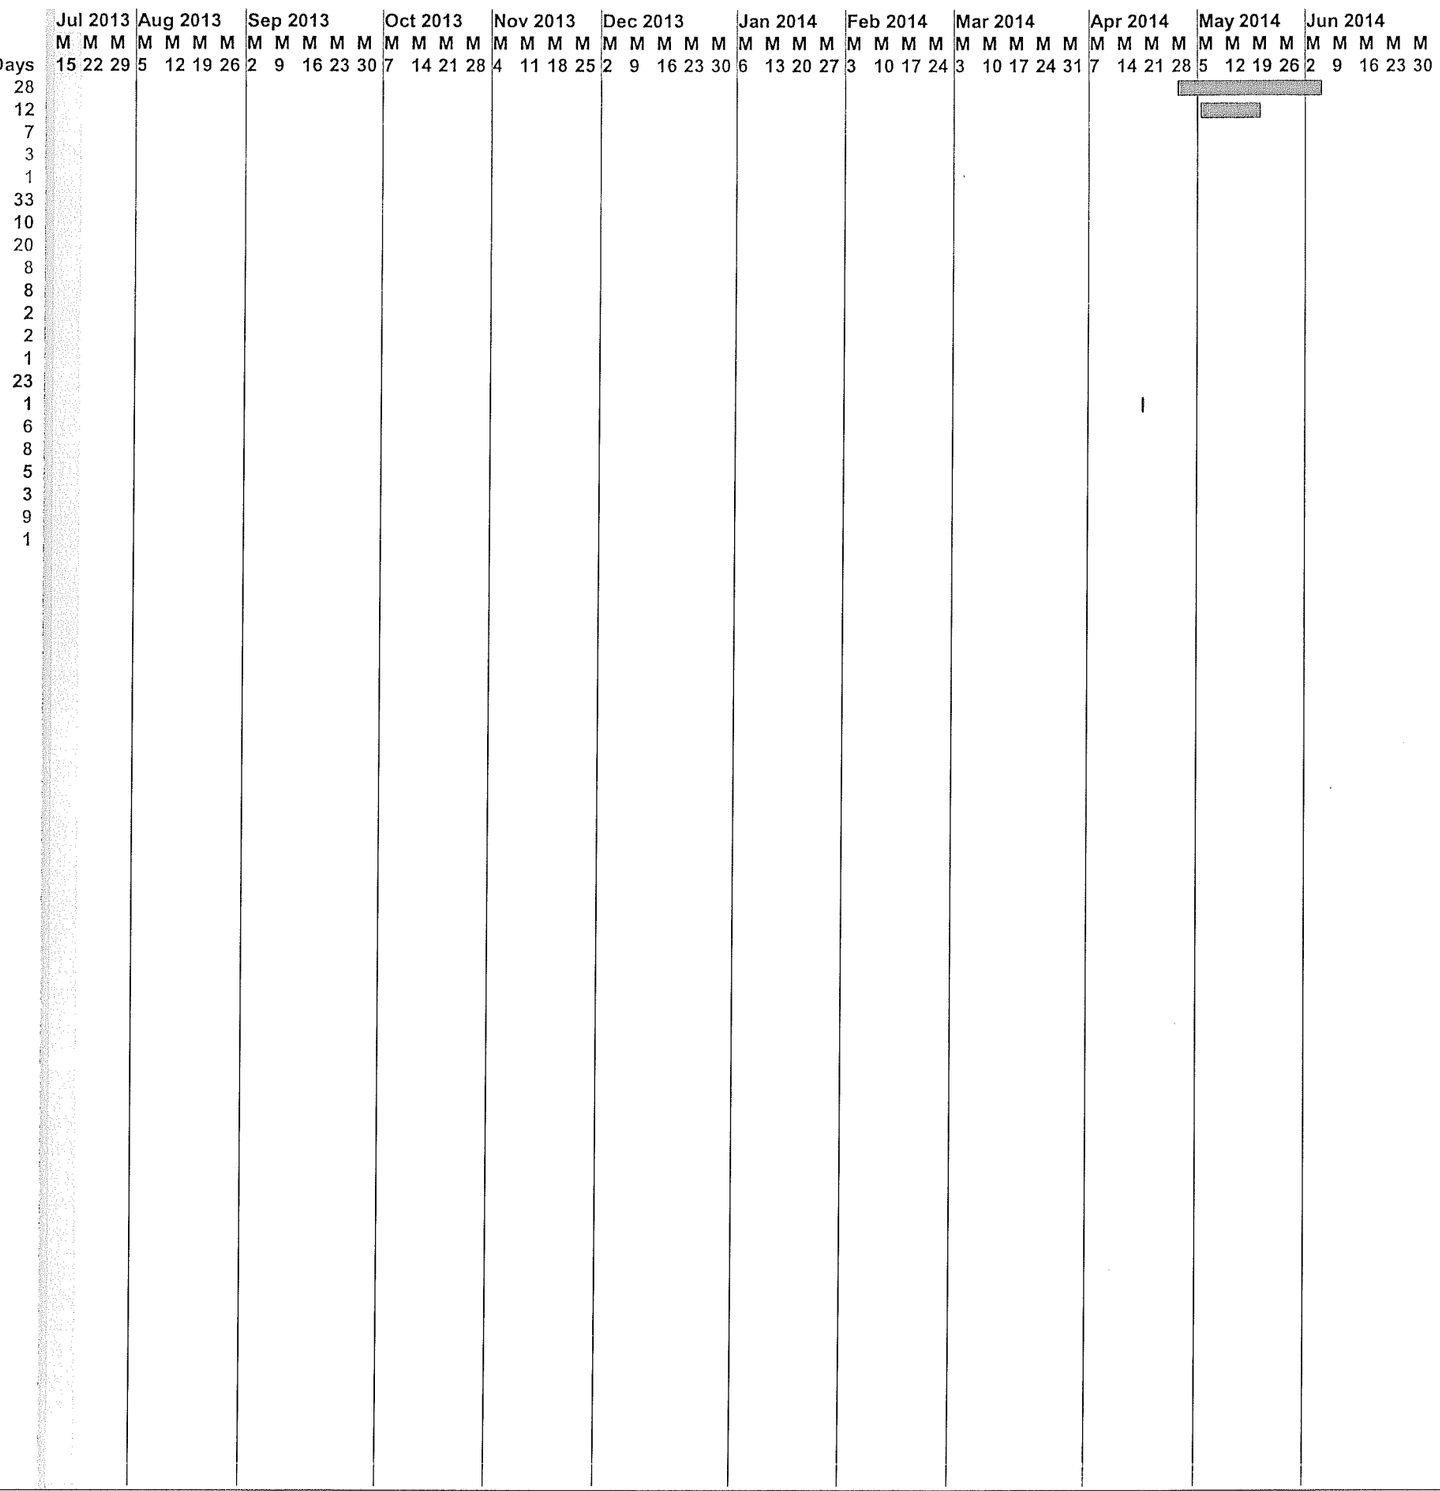
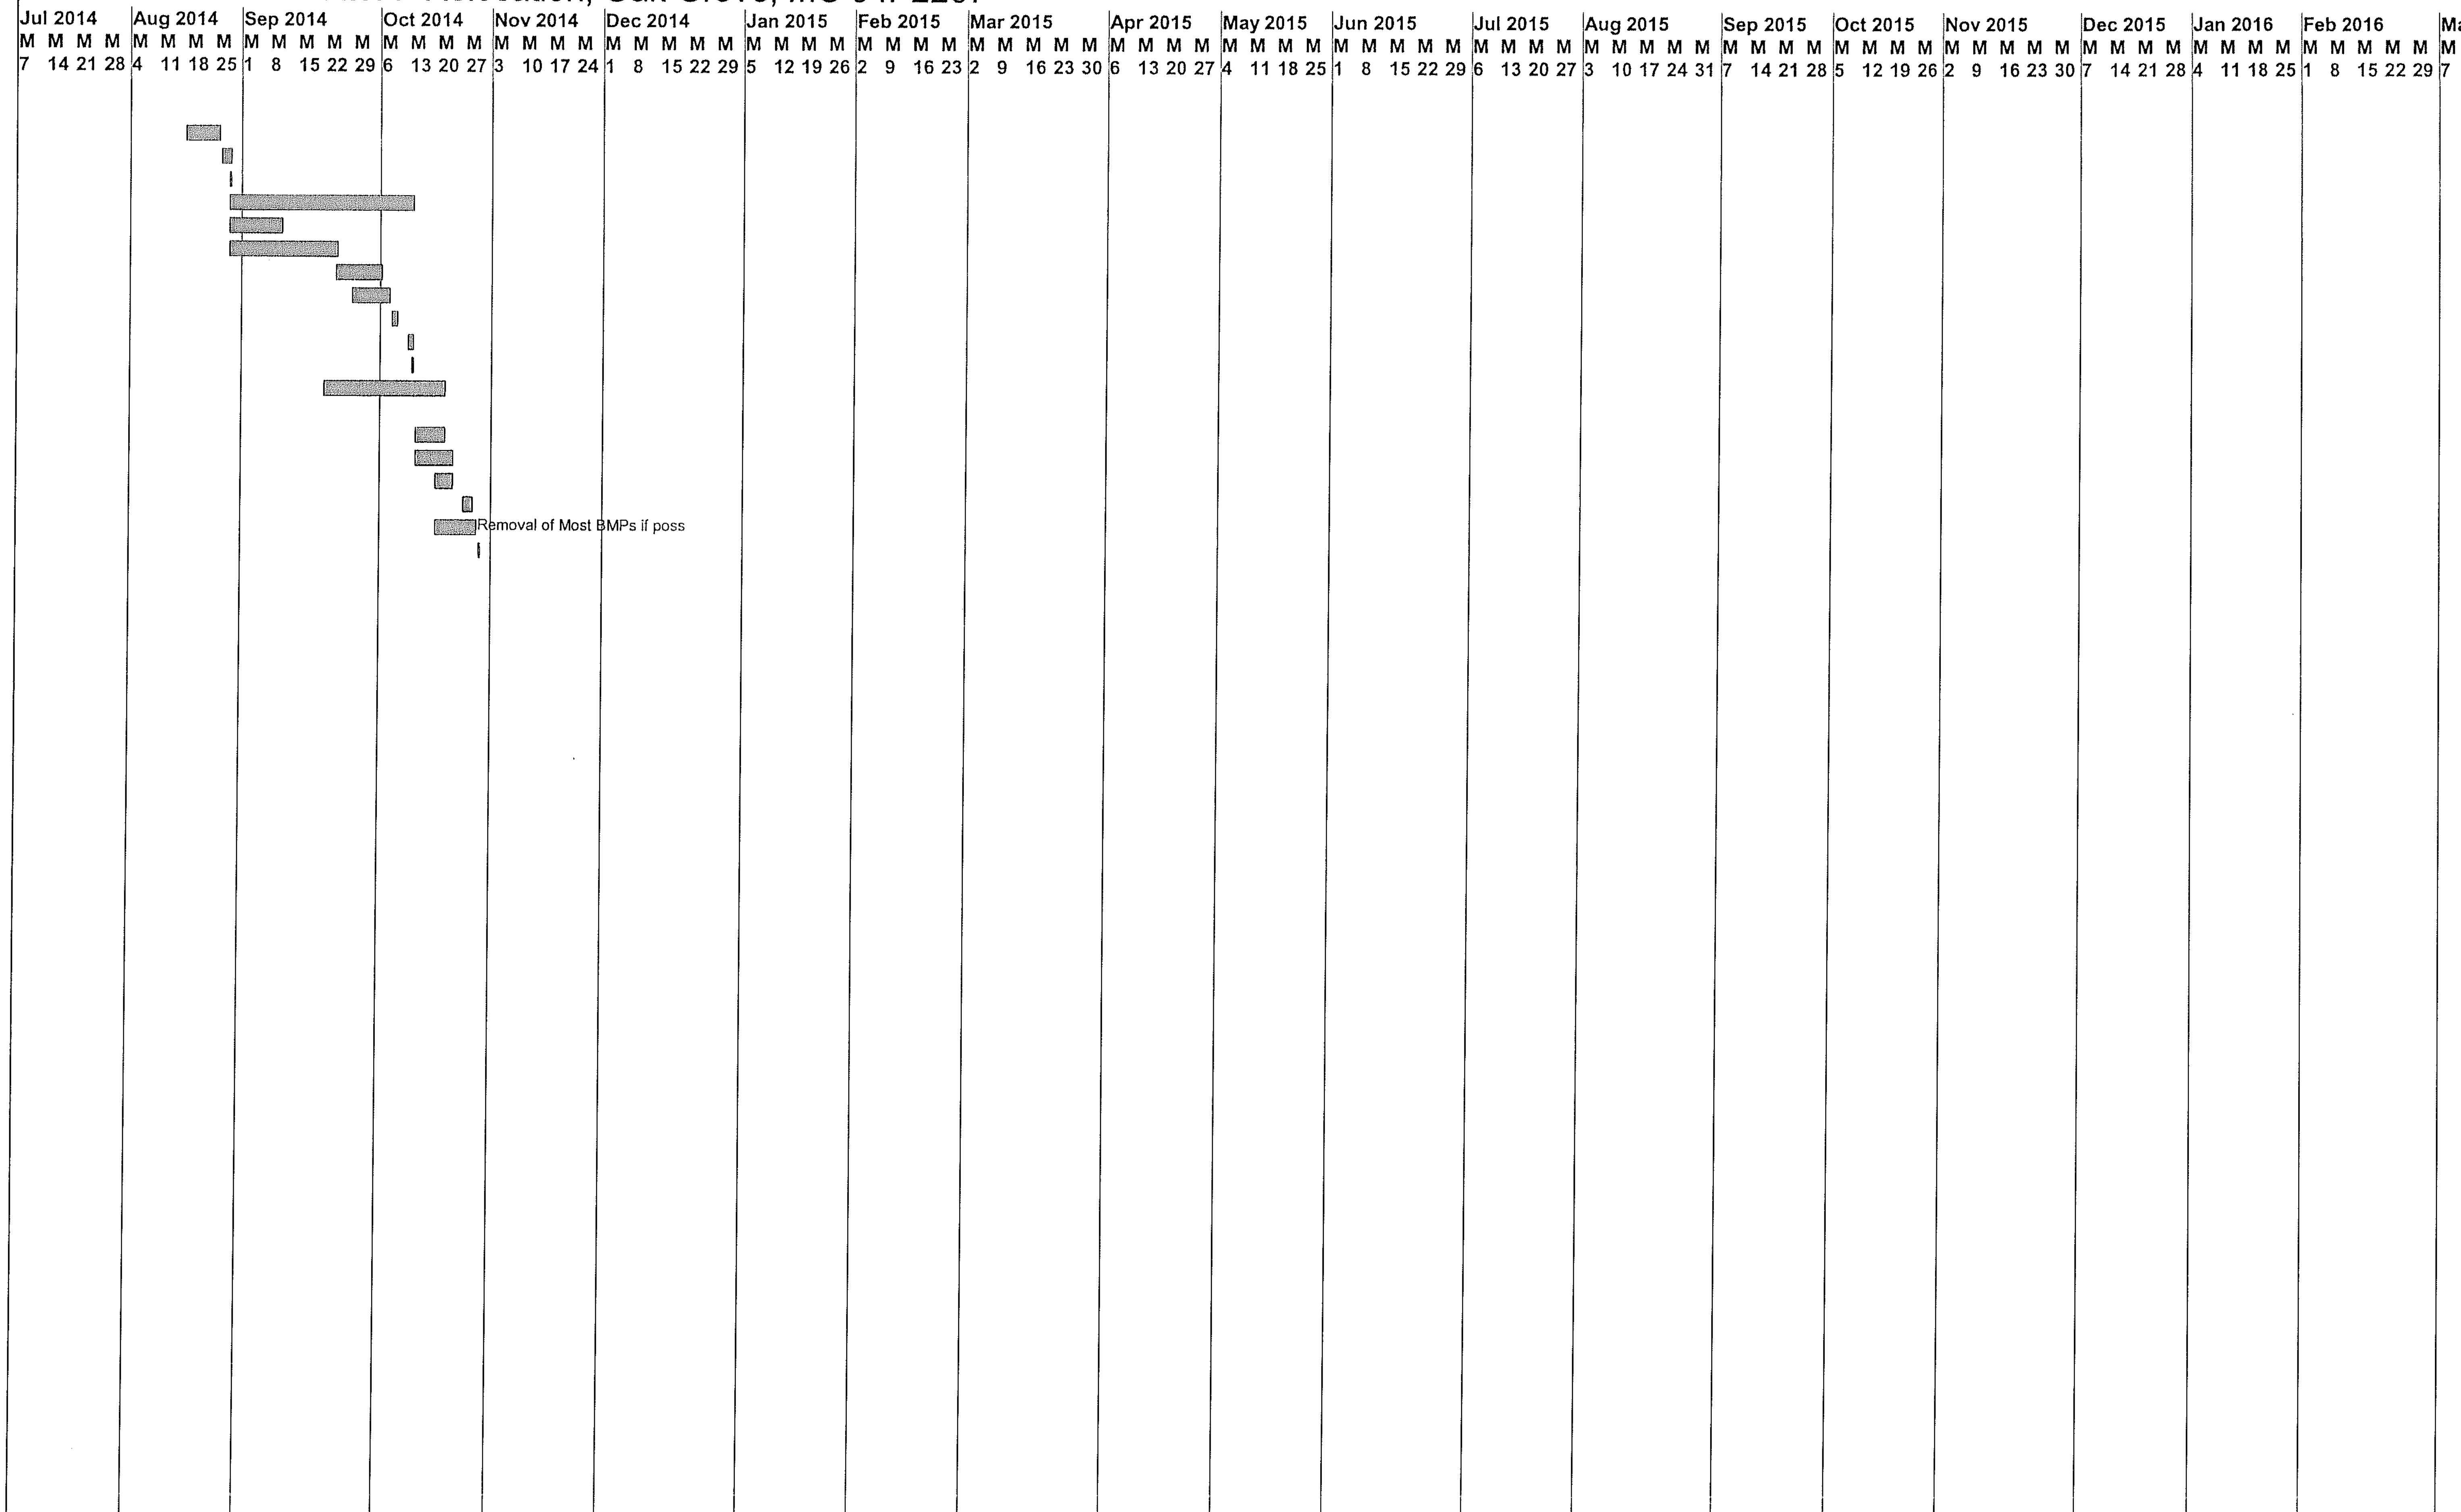
JOB: 13004 Rte. F Relocation, Oak Grove, MO J4P2267
